


PDT Performance

- Regional resourcing greatly enhanced team capability
 - requires continuous high level of communication
- Local sponsor project technical leads enhanced team capability
 - success stems from early involvement and goal setting
- Agencies contributed to planning success and issue resolution
 - team participation is essential to formulation and info exchange
- Detailed and flexible coordination process needed to produce reports
 - frequent team-level and vertical coordination is necessary
- Institutional memory for implementation and O&M challenging
 - district team members essential for design, construction, O&M



PDT Coordination

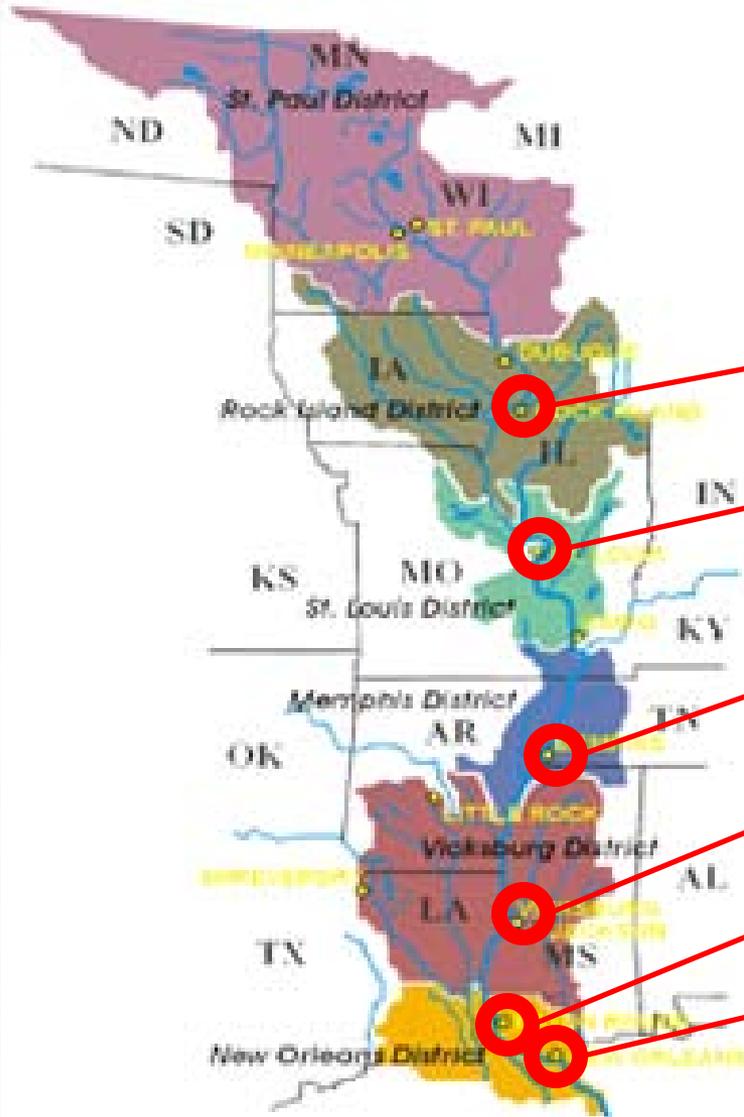

MVR

MVS

MVM

MVD

OCPR

MVN



Possible Process Improvements

- Establish vertical agreement on minimum study timelines
- Agree upon project evaluation or review deviations needed to make timelines
- Obtain vertical concurrence on multi-project report outlines
- Institute a central consistency management function
- Seek policy waivers and deviations as early as possible



MVD Lessons Learned

- Great use of regional and sponsor resources to complete
- Execution of required Cost Share Agreements between parties earlier in the process
- Elevate cost estimating issue to HQUSACE senior level for concurrence earlier in process
- Vertical team alignment on differentiation of authorized TSP and recommendation for NER

